

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)				UCSF ZSFG Lab Project - Contract Schedule										Boldt Company																																		
Activity ID				Activity Name	Start	Finish	Original Duration	Remaining Duration	Total Float	All Activities																																						
										2018				2019				2020				2021				2022				2023																		
										J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A
			R1267	DPW - Street Space / Temporary Occupancy Permit Approv	06-Mar-2020 A	10-Mar-2020	5	0																																								
			R1440	DPH - Permission to Enter Site	12-Mar-2020 A	12-Mar-2020	0	0																																								
			R1500	Escrow	12-Mar-2020 A	05-Jul-2020 A	30	0																																								
			R1206	Dept Urban Forestry - Tree Removal Appealed	16-Mar-2020 A	16-Mar-2020	1	0																																								
			R1272	CITY BUILDING ACCESS DELAY	17-Mar-2020 A	20-Apr-2020 A	5	0																																								
			R1390	OSHA - Excavation Permit	25-Mar-2020 A	16-Apr-2020 A	20	0																																								
			R1405	OSHPD - Fire Line Permit - Review	25-Mar-2020 A	06-Apr-2020 A	20	0																																								
			R1431	BAAQMD - Asbestos Dust Mitigation Plan - Received commr	01-Apr-2020 A	15-Apr-2020 A	10	0																																								
			R1406	OSHPD - Fire Line Permit - Resubmit Package	07-Apr-2020 A	16-Apr-2020 A	20	0																																								
			R1330	SFPUC - Preliminary Storm Water Construction General Pei	13-Apr-2020 A	30-Apr-2020 A	1	0																																								
			R1432	BAAQMD - Asbestos Dust Mitigation Plan - Resubmit	16-Apr-2020 A	20-Apr-2020 A	5	0																																								
			R1406a	OSHPD - Fire Line Permit - 2nd Review	17-Apr-2020 A	18-May-2020	20	0																																								
			R1276	– DBI - Sitework Permit - Appeal Period	20-Apr-2020 A	04-May-2020	15	0																																								
			R1433	BAAQMD - Asbestos Dust Mitigation Plan - Approval	21-Apr-2020 A	04-Jun-2020	30	0																																								
			R1292	DPW - Minor Enc. Perm. for Fire Dept Con. & Signs/Benche	28-Apr-2020 A	18-May-2020	5	0																																								
			R1322	DPW - Sidewalk Improvement Permit - Re-Submit	28-Apr-2020 A	18-May-2020	5	0																																								
			R1358	PG&E - Gas Application - Submit	01-May-2020	15-May-2020	10	0																																								
			R1277	– DBI - Sitework Permit - Appeal Filed	04-May-2020	04-May-2020	1	0																																								
			R1359	PG&E - Gas Application - Approval	18-May-2020	16-Sep-2020	80	0																																								
			R1325	DPW - Sidewalk Improvement Permit - Approval	18-May-2020	19-Mar-2021	9	0																																								
			R1295	DPW - Minor Enc. Perm. for Fire Dept Con. & Signs/Benche	19-May-2020	02-Jun-2020	9	0																																								
			R1406b	OSHPD - Fire Line Permit - Resubmit Package	19-May-2020	15-Jul-2020 A	13	0																																								
			R1286	DBI - Electrical Permit - Submit	22-May-2020	24-Jun-2020	5	0																																								
			R1288	DBI - Plumbing Permit - Submit	22-May-2020	22-Jun-2020	5	0																																								
			R1207	Dept Urban Forestry - Tree Removal Appeal Hearing	28-May-2020	28-May-2020	1	0																																								
			R1350	SFPUC - Water Service Application - Submit	29-May-2020	21-Jul-2020 A	5	0																																								
			R1370	SFPUC - Combined Sewer Permit - Submit	29-May-2020	21-Jul-2020 A	4	0																																								
			R1296	SFASR DPW - Minor Enc. Perm. for Fire Dept Con. - Submi	03-Jun-2020 A	11-Jun-2020	5	0																																								
			R1297	SFASR DPW - Minor Enc. Perm. for Fire Dept Con. - Approv	11-Jun-2020 A	06-Aug-2020	15	0																																								
			R1278	– DBI - Sitework Permit - Appeal Hearing	17-Jun-2020 A	17-Jun-2020	1	0																																								
			R1208	Dept Urban Forestry - Tree Removal Appeal Request for Re	17-Jun-2020 A	17-Jun-2020	1	0																																								
			R1279	– DBI - Sitework Permit - Second Appeal Period	18-Jun-2020 A	02-Jul-2020 A	10	0																																								
R1289	DBI - Plumbing Permit - Approval	23-Jun-2020 A	06-Jul-2020 A	20	0																																											
R1287	DBI - Electrical Permit - Approval	25-Jun-2020 A	06-Jul-2020 A	20	0																																											
R1407	OSHPD - Fire Line Plans - Approval	16-Jul-2020 A	07-Aug-2020	20	0																																											
R1355	SFPUC - Water Service Application - Approval	22-Jul-2020 A	03-Sep-2020	20	0																																											
R1300	DBI - Building Permit Addendum - Submit	03-Aug-2020 A	06-Aug-2020	4	0																																											
R1302	DBI - Building Permit Addendum - Approval	07-Aug-2020 A	03-Dec-2020	20	0																																											
R1408	OSHPD - Fire Line Building Permit - Submit	17-Aug-2020 A	20-Aug-2020	4	0																																											
R1409	OSHPD - Fire Line Permit - Approval	21-Aug-2020 A	27-Aug-2020	10	0																																											
R1310	DPW - Utility Excavation Permit - Submit	28-Aug-2020 A	18-Sep-2020	15	0																																											
R1315	DPW - Utility Excavation Permit - Approval	21-Sep-2020 A	08-Oct-2020 A	20	0																																											
R1260	DPW - Additional Traffic Permit for Construction Approval	20-Nov-2020 A	18-Dec-2020	30	0																																											
R1332	SFPUC - Final Storm Water Construction General Permit	14-Dec-2020 A	29-Dec-2020	10	0																																											
R1356	SFPUC - Waste Water Discharge Permit - Submit	25-Jan-2021 A	29-Jan-2021	5	0																																											

Remaining Level of Effort

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Page 2 of 28

04-Aug-2022

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)			UCSF ZSFG Lab Project - Contract Schedule					Boldt Company																																										
			All Activities																																															
Activity ID		Activity Name	Start	Finish	Original Duration	Remaining Duration	Total Float	2018					2019					2020					2021					2022					2023																	
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A				
		R1357	SFPUC - Waste Water Discharge Permit - Approval	01-Feb-2021 A	19-Feb-2021	15	0																																											
	Subcontracting / Procurement		04-Feb-2019 A	06-Nov-2020	350	0																																												
	R2010	Advertise for Site and Civil	04-Feb-2019 A	18-Feb-2019	10	0																																												
	R2000	RFQ/RFP Preparation for Site and Civil	17-Jun-2019 A	20-Jun-2019	5	0																																												
	R2030	Receive / Review RFP Responses	21-Jun-2019 A	17-Oct-2019 A	15	0																																												
	R2040	Contracting / Onboarding Site and Civil	18-Oct-2019 A	30-Oct-2019 A	20	0																																												
	R2050	Site, Civil Submittals / Approvals	04-Jun-2020 A	23-Oct-2020 A	20	0																																												
	R2060	Site Utility Procurement	08-Sep-2020 A	21-Sep-2020	10	0																																												
	R2055	Rebar Procurement	23-Oct-2020 A	06-Nov-2020	10	0																																												
	Construction		10-Mar-2020 A	28-May-2021	320	0																																												
	R3190	SHELTER IN PLACE DELAY	17-Mar-2020 A	01-May-2020	17	0																																												
	R3500	Project Close-out	24-Apr-2021 A	28-May-2021	19	0																																												
	Site Preparation		10-Mar-2020 A	24-Nov-2020	171	0																																												
	R3025	Remove and Store Loops Sculpture (DPH)	10-Mar-2020 A	12-Mar-2020	2	0																																												
	R3003	Fence Site	12-Mar-2020 A	13-Mar-2020	2	0																																												
	R3000	Mobilization	12-Mar-2020 A	16-Mar-2020	9	0																																												
	R3010	Relocate Café (DPH)	19-Mar-2020 A	19-Mar-2020	9	0																																												
	R3017	— DPH Using Site for COVID19 Testing —	24-Mar-2020 A	21-May-2020	24	0																																												
	R3020	Remove and Store Fountain (DPH)	07-May-2020	15-May-2020	8	0																																												
	R3018	Remove Conex Boxes (DPH)	11-May-2020	15-May-2020	5	0																																												
	R3001	Re-Mobilization	15-Jun-2020 A	19-Jun-2020	5	0																																												
	R3200	Survey Site Control	22-Jun-2020 A	24-Jun-2020	5	0																																												
	R3054	Install Temp Water Meter	09-Jul-2020 A	10-Jul-2020 A	5	0																																												
	R3210	Protect B5 Air Intake	13-Jul-2020 A	14-Jul-2020 A	3	0																																												
	R3004	Install Temp Walkways	15-Jul-2020 A	17-Jul-2020 A	5	0																																												
	R3043	Archeologist Trenches	20-Jul-2020 A	24-Jul-2020 A	5	0																																												
	R3041	Establish Air Monitoring for Dust Control	20-Jul-2020 A	20-Jul-2020 A	1	0																																												

[illegible]

[illegible]

[illegible]

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)				UCSF ZSFG Lab Project - Contract Schedule				Boldt Company																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Activity ID		Activity Name	Start	Finish	Original Duration	Remaining Duration	Total Float	All Activities																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
								2018				2019				2020				2021				2022				2023																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
		B9250	Curtain Wall Procurement at Sawtooth (Aluminum)	19-Jun-2021 A	28-Jan-2022	98	0																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)			UCSF ZSFG Lab Project - Contract Schedule					Boldt Company																														
			All Activities																																			
Activity ID		Activity Name	Start	Finish	Original Duration	Remaining Duration	Total Float	2018				2019				2020				2021				2022				2023										
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
<div></div> <div></div> <div></div> <div></div>	B2090	Contracting / Onboarding	22-Oct-2020 A	15-Jan-2021 ,	20	0																																
	B2100	Submittals / Approvals	26-Jul-2021 A	27-Sep-2021	0	0																																
	B2110	Procurement	27-Sep-2021 A	20-Dec-2021 .	31	0																																
	Casework / Specialties		19-Mar-2020 A	05-May-2022	515	0		Contracting / Onboarding																														
	B2140	RFP Preparation	19-Mar-2020 A	01-Apr-2020 A	5	0		Submittals / Approvals																														
	B2150	Receive / Review RFP Responses	02-Apr-2020 A	05-May-2020	15	0		Procurement																														
	B2160	Contracting / Onboarding	15-Oct-2020 A	01-Apr-2021 A	20	0		05-May-2022 A, Casework / Specialties																														
	B2170	Submittals / Approvals	09-Aug-2021 A	22-Dec-2021 .	26	0		RFP Preparation																														
	B2180	Procurement	25-Mar-2022 A	05-May-2022	30	0		Receive / Review RFP Responses																														
	Roofing		19-Mar-2020 A	11-Nov-2021 .	361	0		Contracting / Onboarding																														
	B2210	RFP Preparation	19-Mar-2020 A	01-Apr-2020 A	5	0		Submittals / Approvals																														
	B2220	Receive / Review RFP Responses	02-Apr-2020 A	05-May-2020	15	0		Procurement																														
	B2230	Contracting / Onboarding	03-Aug-2020 A	31-Aug-2020	20	0		11-Nov-2021 A, Roofing																														
	B2240	Submittals / Approvals	25-Nov-2020 A	24-May-2021	30	0		RFP Preparation																														
	B2250	Procurement - Roofing	09-Jun-2021 A	09-Nov-2021 .	42	0		Receive / Review RFP Responses																														
	B2260	Procurement - Tapered Insulation	20-Aug-2021 A	11-Nov-2021 .	56	0		Contracting / Onboarding																														
	Flooring		19-Mar-2020 A	24-Jun-2022 .	499	0		Submittals / Approvals																														
	B2280	RFP Preparation	19-Mar-2020 A	01-Apr-2020 A	2	0		Procurement - Roofing																														
	B2290	Receive / Review RFP Responses	02-Apr-2020 A	05-May-2020	20	0		Procurement - Tapered Insulation																														
	B2300	Contracting / Onboarding	20-Oct-2020 A	26-May-2021	20	0		24-Jun-2022 A, Flooring																														
	B2310	Submittals / Approvals	26-Aug-2021 A	08-Apr-2022 A	4	0		RFP Preparation																														
	B2320	Procurement	22-Nov-2021 A	24-Jun-2022 .	60	0		Receive / Review RFP Responses																														
	Painting		19-Mar-2020 A	22-Mar-2022 .	457	0		Contracting / Onboarding																														
	B2350	RFP Preparation	19-Mar-2020 A	01-Apr-2020 A	2	0		Submittals / Approvals																														
	B2360	Receive / Review RFP Responses	02-Apr-2020 A	14-Apr-2020 A	20	0		Procurement																														
	B2370	Contracting / Onboarding	15-Apr-2020 A	31-Dec-2020 .	20	0		22-Mar-2022 A, Painting																														
	B2380	Submittals / Approvals	27-Sep-2021 A	04-Mar-2022	56	0		RFP Preparation																														
	B2390	Procurement	25-Jan-2022 A	22-Mar-2022 .	40	0		Receive / Review RFP Responses																														
	Signage		15-Mar-2021 A	18-Nov-2022	420	84	-9	Contracting / Onboarding																														
	B2420	RFP Preparation	15-Mar-2021 A	19-Mar-2021 .	5	0		Submittals / Approvals																														
	B2430	Receive / Review RFP Responses	22-Mar-2021 A	10-May-2021	15	0		Procurement																														
	B2440	Contracting / Onboarding	11-May-2021 ,	21-Oct-2021 A	20	0		18-Nov-2022, Signage																														
	B2450	Submittals / Approvals	25-Feb-2022 A	25-Aug-2022	61	24	-9	RFP Preparation																														
	B2460	Signage Procurement	26-Aug-2022	18-Nov-2022	60	60	-9	Receive / Review RFP Responses																														
	Elevators		03-May-2021 ,	20-Dec-2021 .	122	0		Contracting / Onboarding																														
	B2510	Submittals / Approvals	03-May-2021 ,	21-May-2021	31	0		Submittals / Approvals																														
	B2500	Contracting / Onboarding	25-May-2021 ,	18-Jun-2021 ,	20	0		Contracting / Onboarding																														
	B2520	Elevator Procurement	25-Aug-2021 A	20-Dec-2021 .	36	0		Elevator Procurement																														
	MEP Equipment		01-Jun-2021 A	21-Oct-2021 A	82	0		21-Oct-2021 A, MEP Equipment																														
	B2600	MEP Submittals	01-Jun-2021 A	09-Jun-2021 ,	5	0		MEP Submittals																														
B2610	HVAC AHU and Coils Procurement	10-Jun-2021 A	21-Oct-2021 A	78	0		HVAC AHU and Coils Procurement																															
Sitework		25-Feb-2022 A	14-Mar-2022	10	0		14-Mar-2022 A, Sitework																															
B2525	Contract PG&E Roadway & Utilities Contractor	25-Feb-2022 A	14-Mar-2022	10	0		Contract PG&E Roadway & Utilities Contra																															
Construction		12-Mar-2020 A	03-Apr-2023	772	175	-32	03-Apr-2023																															
Site Preparation		12-Mar-2020 A	14-Oct-2022	656	59	-32	14-Oct-2022, Site Prepa																															
<div></div> Remaining Level of Effort <div></div> Primary Baseline <div></div> Remaining Work <div></div> Actual Level of Effort <div></div> Actual Work <div></div> Critical Remaining Work			Page 10 of 28					04-Aug-2022																														

[illegible]

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)				UCSF ZSFG Lab Project - Contract Schedule										Boldt Company																																	
Activity ID		Activity Name		Start	Finish	Original Duration	Remaining Duration	Total Float	All Activities																																						
									2018			2019				2020				2021				2022				2023																			
									J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A
									03-Jun-2021 A, L3																																						
									Install Inserts on Deck - L3 Area B (East)																																						
									Install Inserts on Deck - L3 Area A (West)																																						
									14-Jun-2021 A, L4																																						
									Install Inserts on Deck - L4 Area B (East)																																						
									Install Inserts on Deck - L4 Area A (West)																																						
									23-Jun-2021 A, L5																																						
									Install Inserts on Deck - L5 Area B (East)																																						
									Install Inserts on Deck - L5 Area A (West)																																						
									06-Jul-2021 A, Roof																																						
									Install Inserts on Deck - Roof Area B (East)																																						
									Install Inserts on Deck - Roof Area A (West)																																						
									19-Aug-2021 A, Concrete																																						
									08-Jun-2021 A, L2 - Area B																																						
									Install Rebar on Decks - L2 Area B (East)																																						
									Pour Concrete on Decks - L2 Area B (East)																																						
									Wet Cure - L2 Area B (East)																																						
									10-Jun-2021 A, L2 - Area A																																						
									Install Rebar on Decks - L2 Area A (West)																																						
									Pour Concrete on Decks - L2 Area A (West)																																						
									Wet Cure - L2 Area A (West)																																						
									17-Jun-2021 A, L3 - Area B																																						
									Install Rebar on Decks - L3 Area B (East)																																						
									Pour Concrete on Decks - L3 Area B (East)																																						
									Wet Cure - L3 Area B (East)																																						
									22-Jun-2021 A, L3 - Area A																																						
									Install Rebar on Decks - L3 Area A (West)																																						
									Pour Concrete on Decks - L3 Area A (West)																																						
									Wet Cure - L3 Area A (West)																																						
									24-Jun-2021 A, L4 - Area B																																						
									Install Rebar on Decks - L4 Area B (East)																																						
									Pour Concrete on Decks - L4 Area B (East)																																						
									Wet Cure - L4 Area B (East)																																						
									30-Jun-2021 A, L4 - Area A																																						
									Install Rebar on Decks - L4 Area A (West)																																						
									Pour Concrete on Decks - L4 Area A (West)																																						
									Wet Cure - L4 Area A (West)																																						
									05-Jul-2021 A, L5 - Area B																																						
									Install Rebar on Decks - L5 Area B (East)																																						
									Pour Concrete on Decks - L5 Area B (East)																																						
Wet Cure - L5 Area B (East)																																															
07-Jul-2021 A, L5 - Area A																																															
Install Rebar on Decks - L5 Area A (West)																																															
Pour Concrete on Decks - L5 Area A (West)																																															
Wet Cure - L5 Area A (West)																																															

Remaining Level of Effort

Actual Level of Effort

Primary Baseline


Actual Work

Remaining Work

Critical Remaining Work

Page 13 of 28

04-Aug-2022

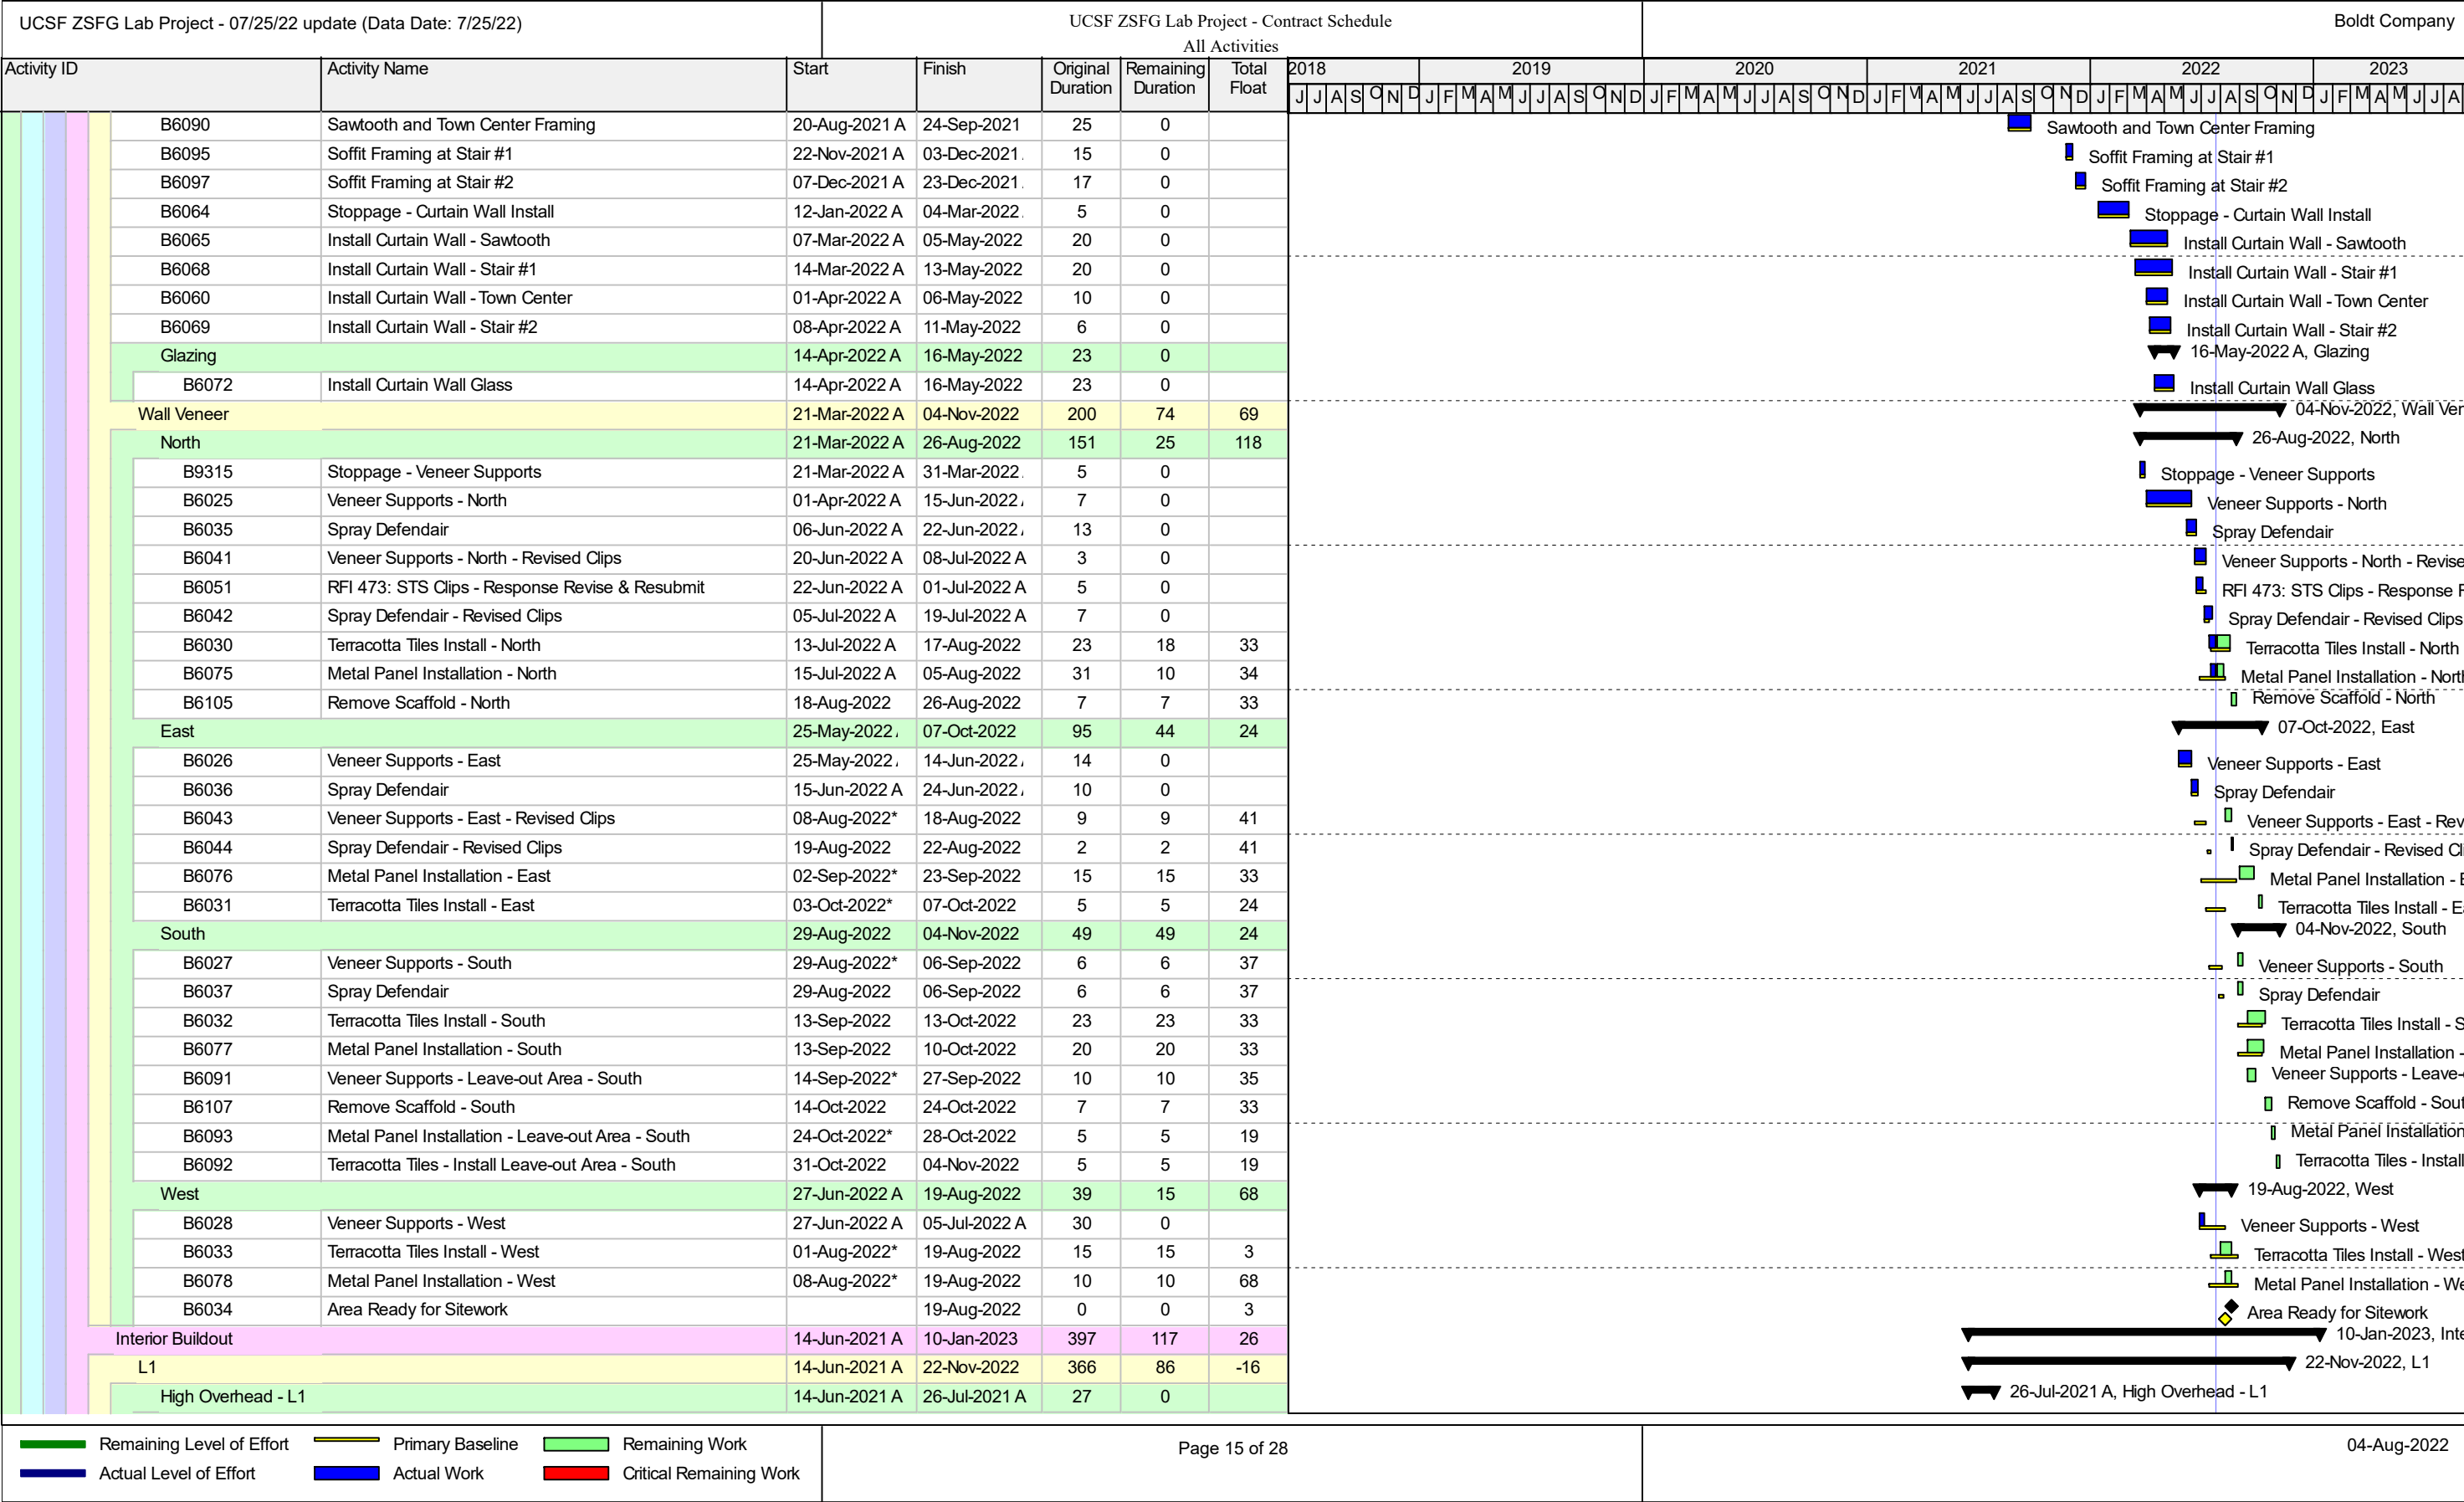

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

UCSF ZSFG Lab Project - 07/25/22 update (Data Date: 7/25/22)			UCSF ZSFG Lab Project - Contract Schedule					Boldt Company																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
			All Activities																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
Activity ID		Activity Name	Start	Finish	Original Duration	Remaining Duration	Total Float	2018					2019					2020					2021					2022					2023																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
								J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M

[illegible]
